

SUBJECT: ACCEPTANCE OF PROJECT – MAIN STREET & PLANO STREET BUS TURNOUTS

SOURCE: Public Works Department - Engineering Division

COMMENT: Hobbs Construction has completed the Main Street & Plano Street Bus Turnouts per plans and specifications. The project consisted of the removal of existing concrete improvements and installation of new concrete improvements allowing a bus to completely pull out of the travel way to access the bus stop location. Concrete pads with bus shelters were installed, adjacent to the back of new sidewalk. Installation of sidewalk between the eastbound Main Street/State Route 190 off ramp and Porterville College was also a part of this project.

Staff carefully tracks construction costs of all Capital Improvements Projects and reports project construction expenditures when the project is accepted by the City Council. On September 17, 2013, City Council authorized expenditure of \$129,211.20 for construction, construction management and quality control services for the Main Street & Plano Street Bus Turnouts. The following itemizes the construction-related costs in two categories: 1) the construction contract, and 2) a combination of construction management and quality control.

- 1) Final construction cost is \$114,131.81.
- 2) Construction management and quality control costs are \$15,304.78.

Total project construction costs equate to \$129,436.59, which is 0.17% more than the \$129,211.20 overall budget approved by Council at the time of award. Funding for the Main Street & Plano Street Bus Turnouts was approved in the 2013/2014 Annual Budget. Federal Transportation Administration Grant (FTA) and a twenty percent (20%) local match are the funding sources for this project. Local Transportation Funds (LTF) is the revenue source for the local share.

Hobbs Construction requests that the City accept the project as complete. Staff reviewed the work and found it acceptable.

RECOMMENDATION: That City Council:


1. Accept the project as complete;
2. Authorize the filing of the Notice of Completion; and
3. Authorize the immediate release of final payment, provided no stop notices have been filed.

ATTACHMENTS: Locator Maps

P:\pubworks\General\Council\Acceptance of Project - Main Street & Plano Street Bus Turnouts - 2014-15-06.doc

Dir BS Appropriated/Funded MS CM JW
ACTING

Item No. 5



NORTH

PROJECT LOCATION

OLIVE AVE.


EASTRIDGE CIR.

PLANO ST.

CITY OF PORTERVILLE
ENGINEERING DIVISION
291 NORTH MAIN STREET
PORTERVILLE, CA. 93257
(559) 782-7462

Plano Bus Turnout Locator Map

OWNER	
APN	
AREA	
ACRES	
SCALE	NO SCALE
DATE	
DRAWN BY	MT
CHECKED BY	

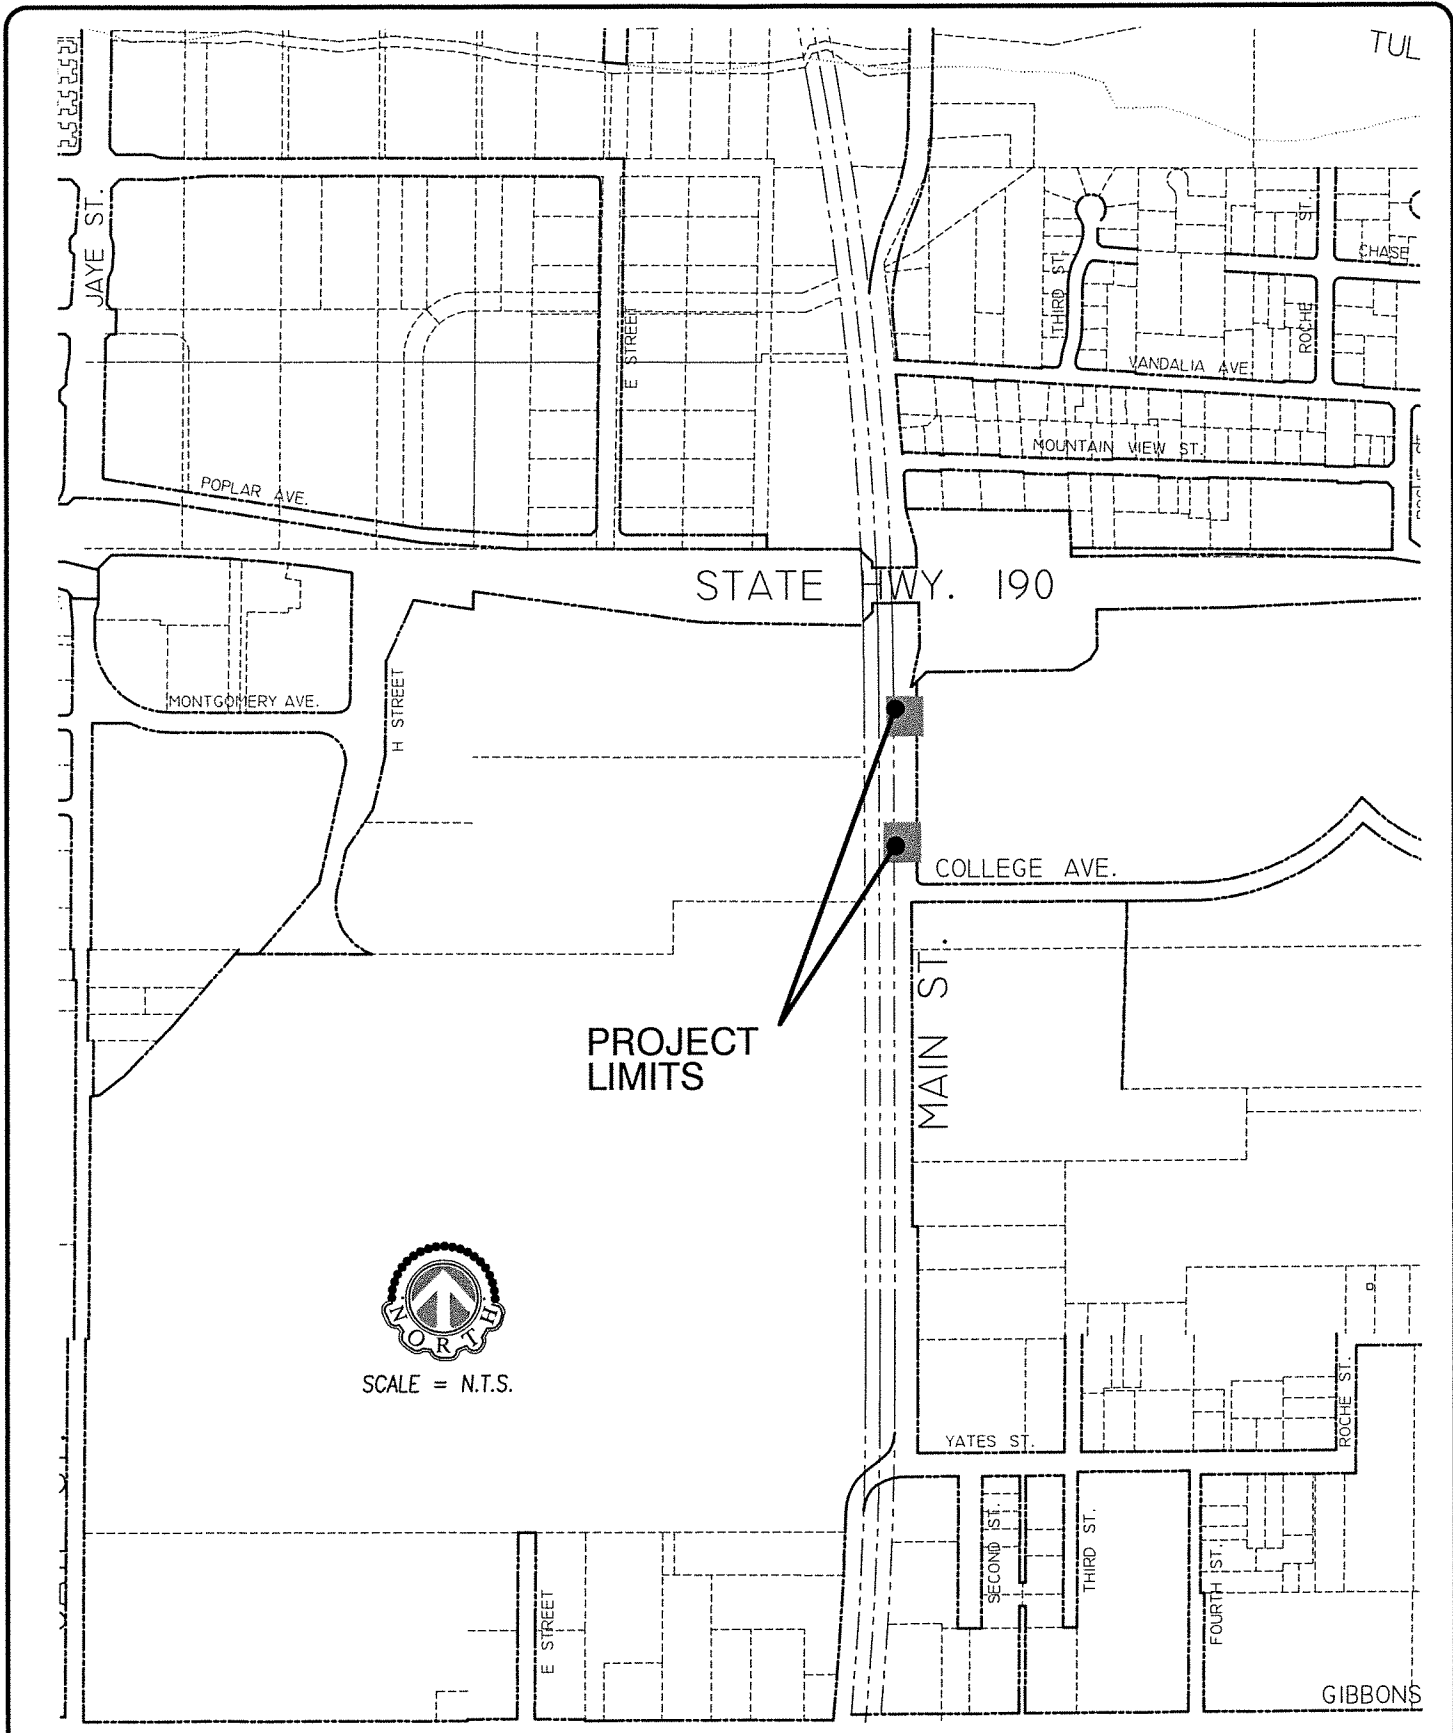

CITY OF PORTERVILLE
 ENGINEERING DIVISION

291 NORTH MAIN STREET
 PORTERVILLE, CA. 93257
 (559) 782-7462

MAIN STREET BUS
 TURNOUT PROJECT
 NEAR PORTERVILLE
 COLLEGE

OWNER	-
APN	-
AREA	-
ACRES	-
SCALE	N.T.S.
DATE	-
DRAWN BY	-
CHECKED BY	-
